

StSI and RbSI Compared

Two New Leaf Earned-Value Indexes Compared

by John M. Nevison, PMP

Introduction

Two recent New Leaf white papers introduce and use two new earned-value indexes. In certain circumstances the two indexes appear to have the same value. The question arises, “Are the two indexes the same?” The answer turns out to be that they are equivalent. However, each index’s formula remains convenient in its own context and awkward in the other’s, so both should be continued.

Note: this white paper is intended as a sequel to two earlier white papers, *Earned Value: Ideas and Exercises*, where the Staffing-to-schedule Index (StSI) is used and *Earned-Value Benchmarks for Re-baselining Your Project* where the Re-baselined Staffing Index (RbSI) is defined and used. If you have not read them, you may want to download them from New Leaf’s site and become familiar with them before continuing. We begin here with the simple example that first appeared in those earlier papers.

A Simple Example

The project shown in Figure 1 below has an original cost, or Budget at Completion (BAC), of 1000 staff-days and an original schedule of 10 months. The calculations begin with the “s-curve” chart of information that depicts the project’s planned value from start to end, and the two actual lines from the project start to the current date. One of the two “actual” lines depicts the actual cumulative cost to date, the other the actual cumulative earned value to date. The last bits of information in the graph are the present date and the planned value to date.

Figure 1. A typical earned value chart.

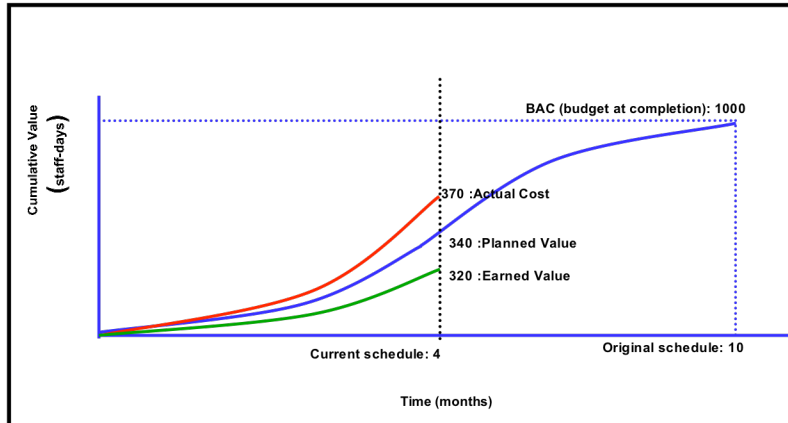


Figure 2. A typical project task list

Task List					
Task name	Plan	Actual	Earned Value	Date completed	
				Planned	Actual
...					
MONTH 3	240	268	238		31-Mar
Pink	16	14	16	2-Apr	5-Apr
Violet	12	16	12	5-Apr	10-Apr
Red	18	22	18	5-Apr	8-Apr
Vermillion	8	10	8	15-Apr	20-Apr
Blue	18	24	18	20-Apr	18-Apr
Brown	8			22-Apr	
Green	10	16	10	22-Apr	28-Apr
Yellow	10			25-Apr	
MONTH 4	340	370	320		30-Apr
Brown*	*			22-Apr	
Yellow*	*			25-Apr	
Beige	2			2-May	
Apricot	2			5-May	
Pink	3			5-May	
...					

A summary of the facts:

1. Original project cost: 1000 staff-days
2. Original project schedule: 10 months
3. Planned value: 340 staff-days at 4 months
4. Actual cost: 370 staff-days
5. Earned value: 320 staff-days
6. Current monthly staff: 5 people

The Staffing-to-schedule Index

At the end of the white paper, *Earned Value: Ideas and Exercises*, the Staffing-to-schedule Index was applied to the planned staff to produce an adjusted staff that would meet the original schedule while preserving the pattern of the original staffing histogram. The index itself was defined in an earlier New Leaf white paper entitled *The Remaining Work Index (RWI) and the Staffing-to-Schedule Index (StSI)*.

In the *Earned Value* paper, the simple example looked like this:

To calculate the number of extra people needed to finish on time, follow these four steps: [New Leaf invented both the RWI and the StSI]

With a planned monthly staff = 5 people:

$$\begin{aligned} 1. \text{ Remaining work index (RWI)} &= \text{remaining planned work} / \text{remaining actual work} \\ &= (1000 - 340) / (1000 - 320) \\ &= 660 / 680 \\ &= .97 \end{aligned}$$

$$\begin{aligned} 2. \text{ Staffing to Schedule Index (StSI)} &= \text{Remaining Work Index} * \text{CPI} \\ &= .97 * .86 = .84 \end{aligned}$$

$$\begin{aligned} 3. \text{ Adjusted staff} &= \text{Planned staff FTEs} / \text{StSI} \\ &= 5 / .84 = 6.0 \text{ staff FTEs} \end{aligned}$$

The Re-baselined Staffing Index

At the end of *Earned-Value Benchmarks for Re-baselining Your Project* the last step in re-baselining the project was to adjust all the remaining staffing to complete the project by the re-baselined date while preserving the adjusted pattern of the original staffing.

The simple example looked like this:

Rebaselined Staffing Index: the RbSI

$$\text{Re-baselined staffing index} = \frac{\text{(Original planned work remaining)}}{\text{(Re-baselined planned work remaining)}}$$

$$\text{RbSI} = \frac{\text{(Original BAC - old current planned value)}}{\text{((Re-baselined cost BAC - new current planned value)}}$$

$$\text{RbSI} = (1000 - 340) / (1156 - 370) = 660 / 786 = .84$$

As with the other earned-value indexes, you divide the original value by the index to arrive at the adjusted value:

Adjusting the Staffing Histogram with the RbSI to Get the Re-baselined Staffing Histogram

$$\text{Original staffing histogram figure} / \text{RbSI} = \text{Re-baselined staffing histogram figure}$$

$$5 \text{ staff FTEs} / .84 = 6.0 \text{ staff FTEs}$$

Two indexes compared

If we look carefully at our two examples, we will find that the StSI is exactly the same value as our RbSI. Is this a coincidence or do the two indexes have a lot in common? In order to find out, we will reduce each definition to a simple set of algebraic terms and compare them.

The two examples below use the following form for their “proofs”:

Statement

= *<reason to transform statement into next statement >*

Next statement

Staffing-to-schedule Index (StSI) is the index that will adjust the original staffing histogram to achieve the full plan on the original schedule and preserve the shape of the staffing histogram.

= *<Using New Leaf’s definition of StSI>*

Remaining Work Index * CPI

= *<Using New Leaf’s definition of Remaining Work Index>*

(Remaining planned work / remaining actual work) * CPI

= *<Using earned-value definitions>*

((Original budget at completion (BAC) – current planned value) /

(Original budget at completion (BAC) – current earned value)) * CPI

= *<Using the definition of CPI>*

((Original budget at completion (BAC) – current planned value) /

(Original budget at completion (BAC) – current earned value)) * (Earned Value / Actual Cost)

= *<Algebraic substitution using: b = BAC, x = Actual Cost, y = Planned Value, z = Earned Value>*

$((b - y) / (b - z)) * (z / x)$

Re-baselined staffing index (RbSI) is the index to adjust the original histogram’s re-baselined pattern in a way that achieves the re-baselined cost in the re-baselined schedule.

= *<Using New Leaf’s definition for the RbSI>*

(Original planned work remaining) / (Re-baselined planned work remaining)

= *<Using earned-value definitions>*

(Original BAC – old current planned value) / (Re-baselined cost BAC – re-baselined current planned value)

= *<Algebraic substitution using b = BAC, x = Actual Cost, y = Planned Value, and definitions for re-baselining from the article, Earned-Value Benchmarks for Re-baselining Your Project>*

$(b - y) / (\text{old-typical-variance-EAC} - \text{old current actual cost})$

= *<Definition of (typical) EAC>*

$(b - y) / ((\text{BAC} / \text{CPI}) - \text{old current actual cost})$

= *<Algebraic substitution using: b = BAC, x = Actual Cost, y = Planned Value, z = Earned Value and Definition of CPI>*

$(b - y) / (b / (z/x)) - x$

= *<algebra part one>*

$(b - y) / ((b*x / z) - x)$

= *<algebra part two>*

$(b - y) / (x*(b/z) - x)$

= *<algebra part three>*

$(b - y) / ((b/z) - 1) * x$

= *<algebra part four>*

$(b - y) / ((b - z) * x / z)$

= *<algebra part five>*

$((b - y) / (b - z)) * (z / x)$

This formula for the SbSI is the same as the StSI. So using the assumptions in the two “proofs,” the two New Leaf indexes are equivalent. In the simple example:

$$\text{RbSI} = (1000 - 340) / (1156 - 370) = 660 / 786 = .84$$

$$\text{StSi} = (1000 - 340) / (1000 - 320) * \text{CPI} = 660 / 680 * (320 / 370) = .97 * .86 = .84$$

The re-baseline and the original plan both have 5.0 planned staff in the next month so the staffing adjustment in both cases is:

$$5.0 \text{ staff FTEs} / .84 = 6.0 \text{ staff FTEs}$$

The above argument was for the common (and conservative) earned-value case where the current cost variance was assumed to be *typical*. In the rare cases when the current cost variance is *atypical*, then the CPI in the Staffing-to-schedule Index becomes 1.0, and the EAC in the Re-baselined Staff Index becomes (BAC – CV). The two indexes remain equivalent. The reader may verify that both indexes work out to be $(b - y) / (b - z)$.

Conclusion: Two Convenient Uses

One might conclude that we want to throw away one of the indexes if they are the same. However, conceptual clarity argues for keeping *both* indexes. Each index’s definition makes sense in the context where it is used. Each definition employs the terms that are immediately at hand when their slightly different staffing questions arise.

Each index —with its independent definition— continues to serve a useful purpose in its own context.

Further Reading

If you want to see what it’s like to use the basic earned-value tools on a real project you may want to read Mark Durrenberger’s *An Earned Value Tutorial*.

If you would like more details on the RWI and the StSI, read John Nevison’s *The Remaining Work Index (RWI) and the Staffing-to-Schedule Index (StSI): How to use New Leaf’s new indexes to adjust staffing and make your schedule*.

If you want to try your hand at calculating basic earned-value figures and other project metrics (including the StSI), read John Nevison’s *Earned Value: Ideas and Exercises*.

If you want to see the original use and definition of the SbSI, read John Nevison’s *Earned-Value Benchmarks for Re-baselining Your Project: Handy benchmarks to help you re-baseline the project*.

All four articles are available on New Leaf’s web site (www.NewLeafPM.com) and **all can be studied to earn additional PDUs**.

About the Author

John M. (Jack) Nevison, PMP is the author of six books and numerous articles on computing and management. During the course of his business career, Nevison has built and sold two businesses, managed projects, managed project managers, and served as both an internal and external consultant to Fortune 100 companies. He is past president of the Mass Bay Chapter of the Project Management Institute (PMI®), a past president of the Greater Boston Chapter of the Association for Computing Machinery (ACM), a certified Project Management Professional (PMP), and a Phi Beta Kappa graduate of Dartmouth.

About New Leaf Project Management

New Leaf is a provider of premier project-management training and consulting. Our comprehensive approach blends training with coaching for sustained practice improvement. We offer project management training for all levels of experience, from novice to veteran including preparation for the Project Management Professional (PMP) Exam. We often customize programs to meet individual client needs. By benchmarking project managers with our proprietary PM Competency Assessment we address our client's greatest needs first.

Score at least 70% correct on the questions below and earn PDUs! See next page for details.

PDU Questions: StSI and RbSI Compared

(\$9.95 for 1 PDU)

1. The Budget at Complete (BAC) is in the final algebraic formulas for which indexes?
 - a. StSI
 - b. RbSI
 - c. Neither
 - d. Both

2. The current planned value is in the final algebraic formulas for which indexes?
 - a. StSI
 - b. RbSI
 - c. Neither
 - d. Both

3. The current actual cost is in the final algebraic formulas for which indexes (with a *typical* assumption)?
 - a. StSI
 - b. RbSI
 - c. Neither
 - d. Both

4. The current actual cost is in the final algebraic formulas for which indexes (with a *atypical* assumption)?
 - a. StSI
 - b. RbSI
 - c. Neither
 - d. Both

5. The current staffing is in the final algebraic formulas for which indexes (with a *typical* assumption)?
 - a. StSI
 - b. RbSI
 - c. Neither
 - d. Both

6. To adjust a current periodic staffing the formula using the StSI is?
 - a. Current staff FTEs / StSI
 - b. Current staff FTEs + StSI
 - c. Current staff FTEs - StSI
 - d. Current staff FTEs * StSI

7. To adjust a current periodic staffing the formula using the RbSI is?
 - a. Current staff FTEs / RbSI
 - b. Current staff FTEs + RbSI
 - c. Current staff FTEs - RbSI
 - d. Current staff FTEs * RbSI

StSI and RbSI Compared

\$9.95 for 1 PDU

If you score 70% or more correct answers, a PDU certificate will be e-mailed to you. These PDUs count as "Category 3: PMI/R.E.P. Educational Activities" and are not limited for CCR/PMP recertification purposes. To receive your PDUs, please fill in the information below (fields are required).*

* Name (as it appears on your credit card)

* Phone Number

* Account Number: MasterCard Visa
(For multiple tests, fill in required info once.)

* E-mail address

Address

* Expiration Date: (mm-yy)

City

State/Province

Zip Code

Country

How did you hear about our PDU White Papers?

Approximately how many hours did it take you to read the article and take the test?

**Please mail the answer sheet(s) with payment to:
(or e-mail to info@newleafpm.com
or fax to +978-369-9009 — call first)**

**PDU White Papers
New Leaf Project Management
500 Thoreau Street
Concord, MA 01742 USA**
